

North Wall Toe Piling Phase 2

Southwold, Suffolk

Update – week ending 23rd May 2025

Following on from our most recent updates, please find below some additional information about the works progress. Please do get in touch if you have any concerns or need further information.


- Deliveries of the steel sheet piles have been received.
- On Thursday 22nd May a total of 62 piles have been installed safely. We anticipate installation of a further eight piles on Friday 23rd May.

Works taking place from Tuesday 27th May:

- Further deliveries of the steel sheet piles.
- Continuing to install the steel sheet piles.

Thank you for your patience while these works are taking place. Please continue to follow the traffic management system in the car park.

Photos below showing the installed steel sheet piles. Once the gap between the existing and new steel sheet piles has been filled with concrete, they will be cut to the same level as the existing steel sheet piles.

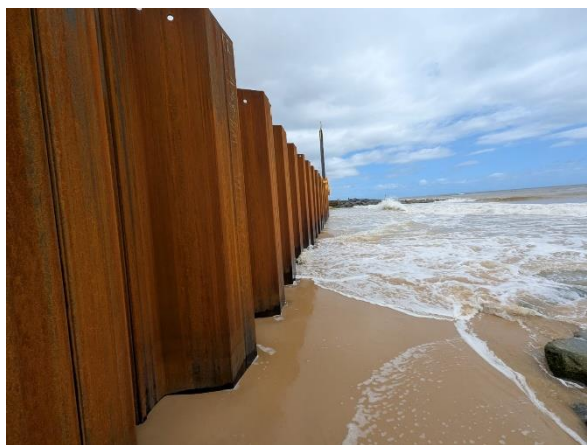

Contact us

Coastal Management service, Riverside, 4 Canning Road, Lowestoft, NR33 0EQ

If you would like this factsheet in another format, please let us know by emailing:

coastalmanagement@eastsuffolk.gov.uk

Follow us on social media

X: @EastSuffolk

Facebook: @EastSuffolkCouncil

Instagram: @eastsuffolkcouncil

www.eastsuffolk.gov.uk
