North Wall Toe Piling Phase 2 Southwold, Suffolk

Update – week commencing 5th May 2025

Following on from our most recent updates, please find below some additional information about the works progress. Please do get in touch if you have any concerns or need further information.

- Temporary site compound has been set up.
- Deliveries of the steel sheet piles have been received.
- A reaction stand was set up and the four shorter dummy piles were installed to provide initial
 guidance for the silent press piler. After some of the full length piles were installed, the dummy
 piles were removed.
- Whilst wind speeds have been exceeding safe working conditions for installing the piles, 11 full length piles were able to be installed.

Works taking place from Monday 12th May:

- Further deliveries of the steel sheet piles.
- Continuing to install the steel sheet piles.


Parking

A temporary site compound and traffic management system have been set up in Southwold Pier car park. Both Southwold Pier and Southwold Beach car parks remain open. A map of the impacts on car parking is on page 2 of this update.

The car park south of the working area and motorhome parking are available as usual. A single lane two way access with priority designations is now in place past the motorhome parking to allow access to the motorhome turning area and Southwold Beach car park. The one way system remains in place as usual south of the working area. Deliveries requiring vehicles too large to use the one way system will be escorted through the car park by traffic marshals.



North Wall Toe Piling Phase 2 Southwold, Suffolk

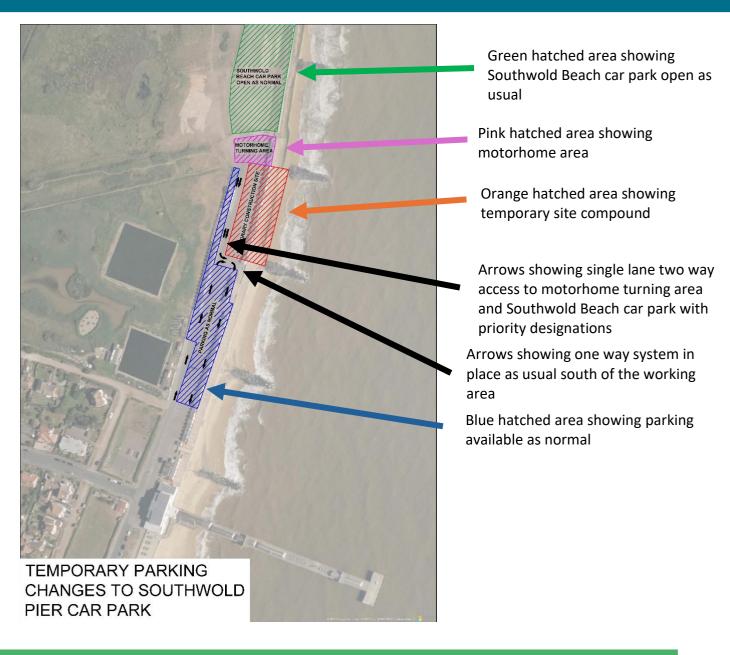

Contact us

Coastal Management service, Riverside, 4 Canning Road, Lowestoft, NR33 0EQ

If you would like this factsheet in another format, please let us know by emailing: coastalmanagement@eastsuffolk.gov.uk

Follow us on social media

X: @EastSuffolk

Facebook: @EastSuffolkCouncil Instagram: @eastsuffolkcouncil

www.eastsuffolk.gov.uk

